Loop testing progress

28 HW I/O and 26 loop references completed; 36 CPCLs recorded in CWA (25 OK, 11 PB). System 53 joined the workfront with 13 loops field complete.

Data through 17 Oct | Report 18 Oct | 8 daily reports

Loop refs commenced	Field complete	Recorded OK/PB in CWA	Punch B share of CWA	Awaiting CWA close	HW I/O yesterday
215	188	197	43%	11	28
+30	+26	+36	-3 pts	-9	-2








What the data says

Calculated from the daily figures

Punch B is growing faster than clean closures

Punch B went from 20% of CWA records on 11 Oct to 43% now. Since 14 Oct, PB rose by 40 and OK by 33. On 17 Oct OK outpaced PB (+25 vs +11) after 3 days of PB leading, so the PB share fell.

85
PB records

The CWA backlog is coming down

Field-complete loop references still showing OS in CWA peaked at 20 on 16 Oct and stand at 11 now. A further 18 partially tested references are already OK/PB in CWA, which is the opposite mismatch.

29
refs to reconcile

Instrument I/O rate holds up without System 82

Without System 82 electrical, completed I/O went 20 → 24 → 30 → 28 over 14 Oct, 15 Oct, 16 Oct, 17 Oct. System 82 accounted for 50 of 70 and 56 of 80 on the high days, so the lower totals since are the 82 work finishing, not a slowdown.

28
non-82 I/O, 17 Oct

Work in progress keeps widening

27 commenced loop references are not field complete (19 partially tested, 8 with no I/O yet), up from 4 on 11 Oct. Field completions average 22.5 a day, so finishing commenced loops before opening new ones would show up quickly in CPCL closures.

27
open loop refs

Figures do not quite add up


Field complete – awaiting CWA + partial-already-in-CWA comes out 1, 1, 1, 2, 2 below the CWA total on each day from 13 Oct. Closures credited to the day also differ from the CWA change: 15 Oct 21 vs 22; 16 Oct 17 vs 15. Worth a tracker vs CWA check.

2
unexplained CPCLs

THROUGHPUT


Cumulative progress

Loop references / CPCLs, by day the figures describe

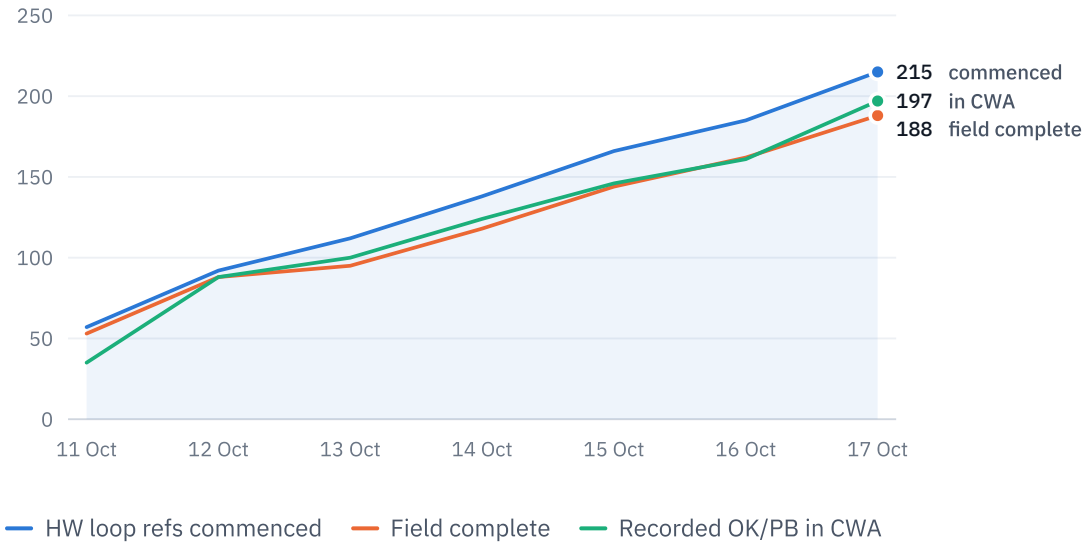

HW I/O completed per day


Individual signals, by system

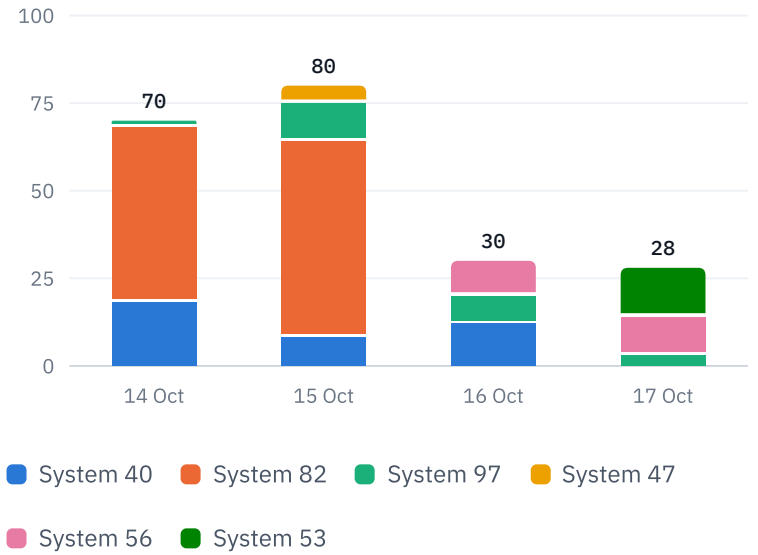

CWA CLOSE-OUT


CPCLs recorded in CWA

OK vs Punch B, with PB share

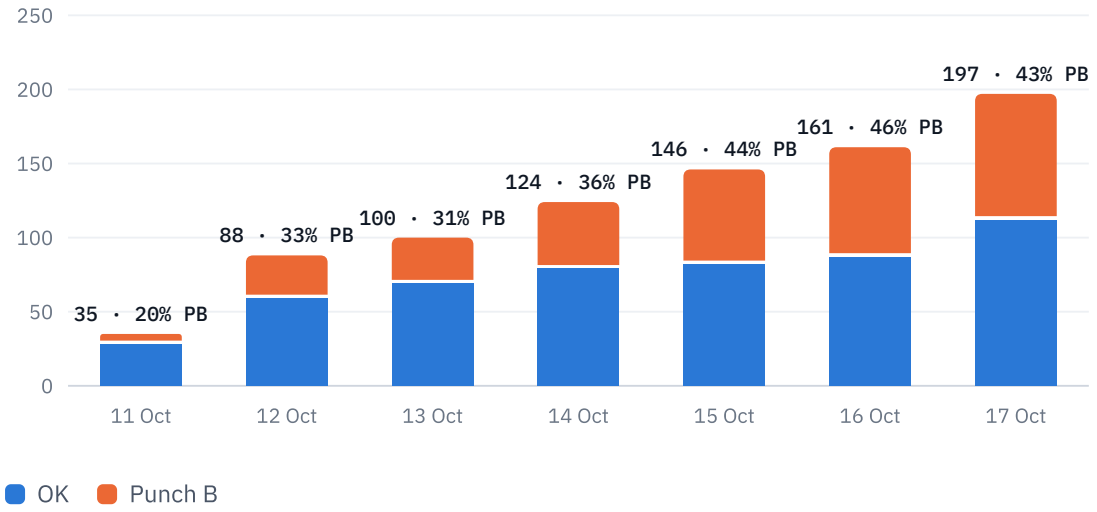


Pipeline today

Through 17 Oct

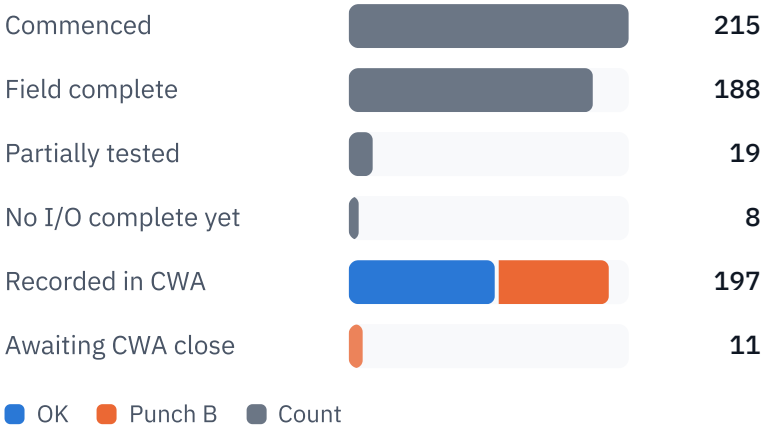

Reconciliation backlog

Tracker and CWA disagree on these loop references

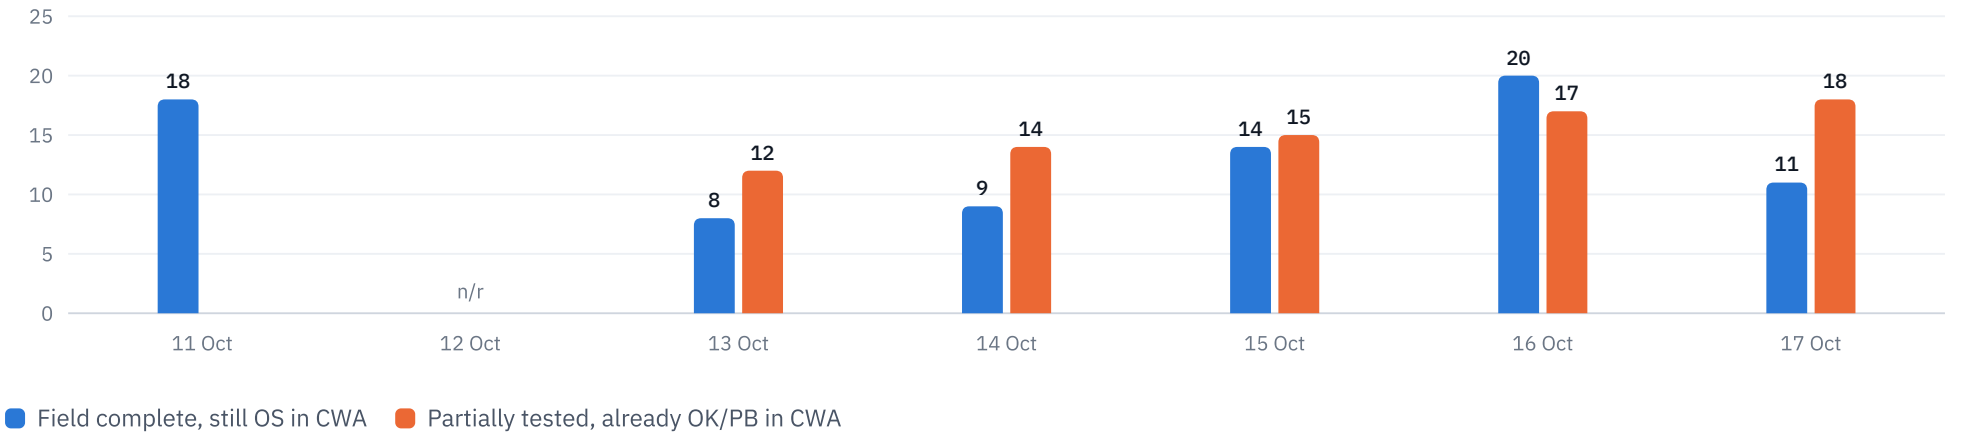

SYSTEMS

Workfront by system

Status from the latest report · I/O total for 14–17 Oct

40
Cooling Medium

Active · valve issue

38 I/O 14–17 Oct · 13 Oct remaining: 14 refs / 67 I/O

Five more CPCLs OK/PB on 17 Oct, including outstanding loop 40-0103. Valve command/feedback discrepancies still under investigation; Rotork checks confirmed DDC address 50 and 2% deadband. Valve response and approved settings to be verified before acceptance.

47
System 47

Active

5 I/O 14–17 Oct

Four more CPCLs recorded OK/PB on 17 Oct. Continue outstanding I/O and CWA / Punch B close-out.

50
Seawater

Active · CWA mismatch

No I/O reported 14–17 Oct · 13 Oct remaining: 9 refs / 25 I/O

Four field-complete CPCLs under 5001-C04 still OS in CWA. Serial/VMS CPCL linkage also needs updating so serial signals sit under their parent loops.

53
System 53

Active

14 I/O 14–17 Oct

Brought in 17 Oct: 14 I/O, 13 loop references field complete and 13 CPCLs OK/PB. Package preparation for functional commissioning next.

56
System 56

Active

21 I/O 14–17 Oct

11 I/O and 10 CPCLs OK/PB on 17 Oct. Six field-complete loops still show OS in CWA.

64
System 64

Active · readiness

No I/O reported 14–17 Oct · 13 Oct remaining: 4 refs / 12 I/O

Available HW testing alongside Systems 47 and 87, subject to field and workstation readiness.

82
Electrical

Digital tests 19 Oct

106 I/O 14–17 Oct

106 I/O completed on 14–15 Oct. Digital functional testing planned from Mon 19 Oct, subject to simulation checks, switching arrangements and Siemens/operator support.

87
System 87

Active

No I/O reported 14–17 Oct · 13 Oct remaining: 6 refs / 21 I/O

Outstanding HW loops, Siemens interface coordination and Punch B close-out.

97
System 97
Active

`24 I/O 14–17 Oct`

Started 14 Oct; 3 I/O and 4 CPCLs OK/PB on 17 Oct. Expanding the workfront and clearing outstanding punches.

70/72
Systems 70 / 72
Readiness

`No I/O reported 14–17 Oct`

RFCC, energisation, vendor readiness and interface-testing preparations.

85/86
Systems 85, 86
Readiness

`No I/O reported 14–17 Oct`

Preparing to enter the workfront as RFCC, energisation and vendor readiness allow.

CONSTRAINTS & LOOK-AHEAD

Constraints log

Raised in the daily reports

CONSTRAINT	RAISED	STATUS	LATEST
Valve command vs feedback	16 Oct	Open	Commanded and actual positions differ on 40TV0044A, 40FV0082A and others. Rotork DDC settings (address 50, Modbus RTU, 2% deadband) obtained on 17 Oct; repeat functional testing needed before closure.
SCADA / HMI availability	13 Oct	Open	Siemens downloads interrupted HMI and reactivated dormant alarms. Improved by 14 Oct, but the Level 7 system was down for several hours on 16 Oct PM.
5001-C04 CWA records	13 Oct	Open	Four previously OK System 50 CPCLs still show OS in CWA (unchanged in the 18 Oct report).
Serial/VMS CPCL linkage	17 Oct	Open	Existing serial signals need linking to their parent loops in the CPCL records (System 50).

Coming up

Dates in the 18 Oct report

19 Oct — in 1 day

System 82 digital functional testing

Electrical, Siemens and loop-testing teams to agree switching and test boundaries.

19 Oct — in 1 day

CC2/CC3 integration forecast

Target cob Monday, including advance notice to Siemens for ADG packages.

26 Oct — in 8 days

Night shift starts

Additional testing team, subject to resources and workstations.

CONSTRAINT	RAISED	STATUS	LATEST
Wi-Fi connectivity	13 Oct	Partly fixed	Level 1A stays improved. Level 7 still needs work after the 16 Oct workstation outage and lost testing time.
Operator access for DO activation	13 Oct	Partly fixed	Reported resolved on 14 Oct; every report since still asks Siemens for operator permissions and DO activation support.
System 82 digital input state / HMI mapping	9 Oct	Partly fixed	4 CPCLs and 52 I/O held until 14 Oct. The panels were then field complete and recorded PB; digital functional testing comes next.
RIO cabinet I/O cards	9 Oct	No update	Card issues in some RIO cabinets were under investigation. No later report mentions them.
Alarm list / descriptions	11 Oct	Resolved	Alarm list available again on 14 Oct. Loops tested earlier need alarm re-verification.
Siemens operators at workstations	13 Oct	Resolved	Siemens operators at each workstation from 14 Oct.

LOOP REGISTER

Planned loop lists

Signal rows from the 9 Oct and 12 Oct look-ahead tables

9 Oct list: 43 signals across 42 loops · 12 Oct list: 158 signals across 71 loops. The full searchable lists are in the online dashboard and the offline page.

DATA NOTES

- Figures are transcribed from the 'Loop Testing Status' tables in each daily look-ahead email.
- progressThrough is the day the figures describe; reportDate is the day the email was sent.
- null means the report did not state that figure.
- From the 15 Oct report onwards the first row was renamed from 'CPCLs Commenced (Instrument I/O)' to 'HW Loop References Commenced' and described as a reconciled tracker total.
- The 15 Oct report says 22 additional OK/PB records, but its per-system table adds up to 21.
- The 13 Oct report shows 0 field-complete CPCLs awaiting CWA close. The next day, 4 previously OK System 50 CPCLs (5001-C04) appeared as OS.
- The 12 Oct list holds 158 signal rows across 71 loops (Systems 40, 50, 64). The 9 Oct list holds 43 AI signals, all Full RFCC, on RIO cabinets 87JF121–123.
- System 82 figures are electrical panel I/O, at about 20 I/O per CPCL. Instrument loops have 1–5 I/O each, so I/O counts and CPCL counts trend differently.

Source: “Loop test daily Look Ahead” email thread, 9–18 Oct 2026. Copy generated 2026-10-19 from data through 2026-10-17.

CPCL = commissioning check list · CWA = completions system · OK / PB / OS = accepted / Punch B / outstanding
